



## Daily Log: Thursday 6/20/2024



Daily Log Completed

The Daily Log was completed by Noah Amidon on Sat, Jun 22, 2024 at 07:29 AM MDT.

### WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
51°F	55°F	53°F	0.00 in.	0.00 in.	0.00 in.	53%	57%	60%	38°F	8.2 mph	12 mph	22 mph

### DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Clear 51°F	Clear 60°F	Cloudy 68°F	Cloudy 57°F	Clear 63°F	Cloudy 52°F

### OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	07:40:00 AM	No						

### MANPOWER LOG

8 Workers | 80.0 Man Hours

No.	Contact/Company	Workers	# Hours	Man Hours	Location
1	Engineered Demolition, Inc	6	10.0	60.0	
<b>Comments:</b> Continuing demo at roof overhangs and cutting out opening at 212A. Also demoed siding sections at north and west sides on first floor to check for water damage to Dens Glass. The first floor densglass was found to be dry with no mold damage where demoed.					
2	PG Arnold Construction	2	10.0	20.0	
<b>Comments:</b> Waterproofed the first floor siding demo.					
		<b>8</b>	<b>80.0</b>		

Manpower Log's Attachments:

1. Engineered Demolition, Inc

---



[FA064B77-7841-4A28-A42E-2B0DE4BBC83C.jpg](#)



[4F5D6767-FE20-4A91-B1D5-45B2525EC147.jpg](#)



[42C7D3C5-363F-4082-8AB2-96E7E3EE2C4A.jpg](#)



[570ED1BA-4C75-43E1-ABC2-E8E3481D765D.jpg](#)



[A94FF98A-0FC0-401F-BB19-384CE855CF1A.jpg](#)




[E2989C82-4324-4237-982E-E1603BA487A3.jpg](#)



[AB69FEE1-981C-4495-8803-D0029AD4D5E9.jpg](#)



[0C9A31FF-F4BF-4196-A5BA-0D095043EF19.jpg](#)

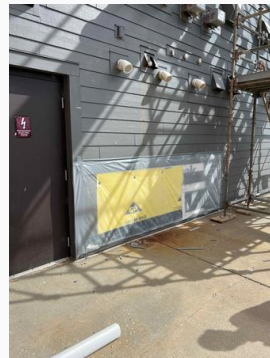

[6FCBD1C9-6A19-4F54-BFC6-5257BB1F7C97.jpg](#)

### NOTES LOG

No.	Issue?	Location	Comments
1	No		Walked with Dm Construction to review the masonry scope.
